ALASKA DISTRICT

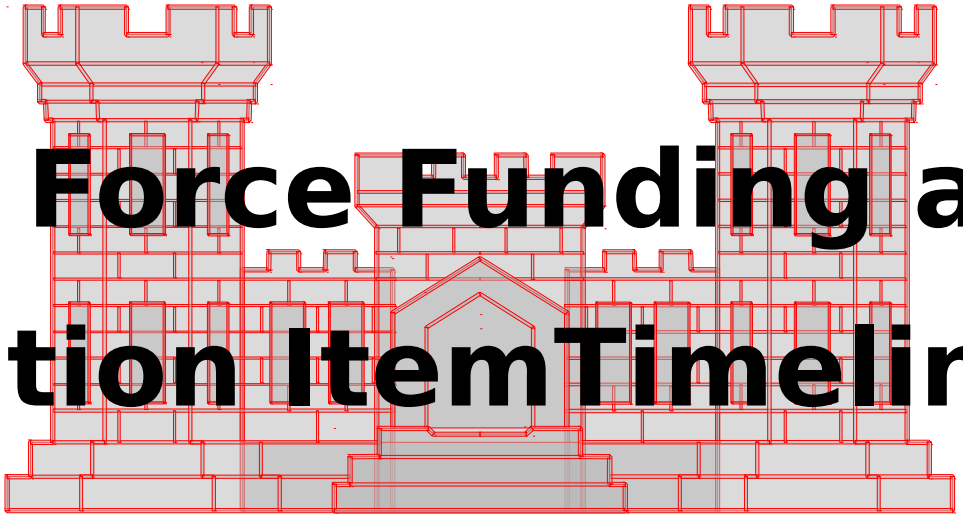

Air Force Funding and Action Item Timelines

Alaska District

AF REIMBURSABLE FUNDING CYCLE

ALASKA DISTRICT

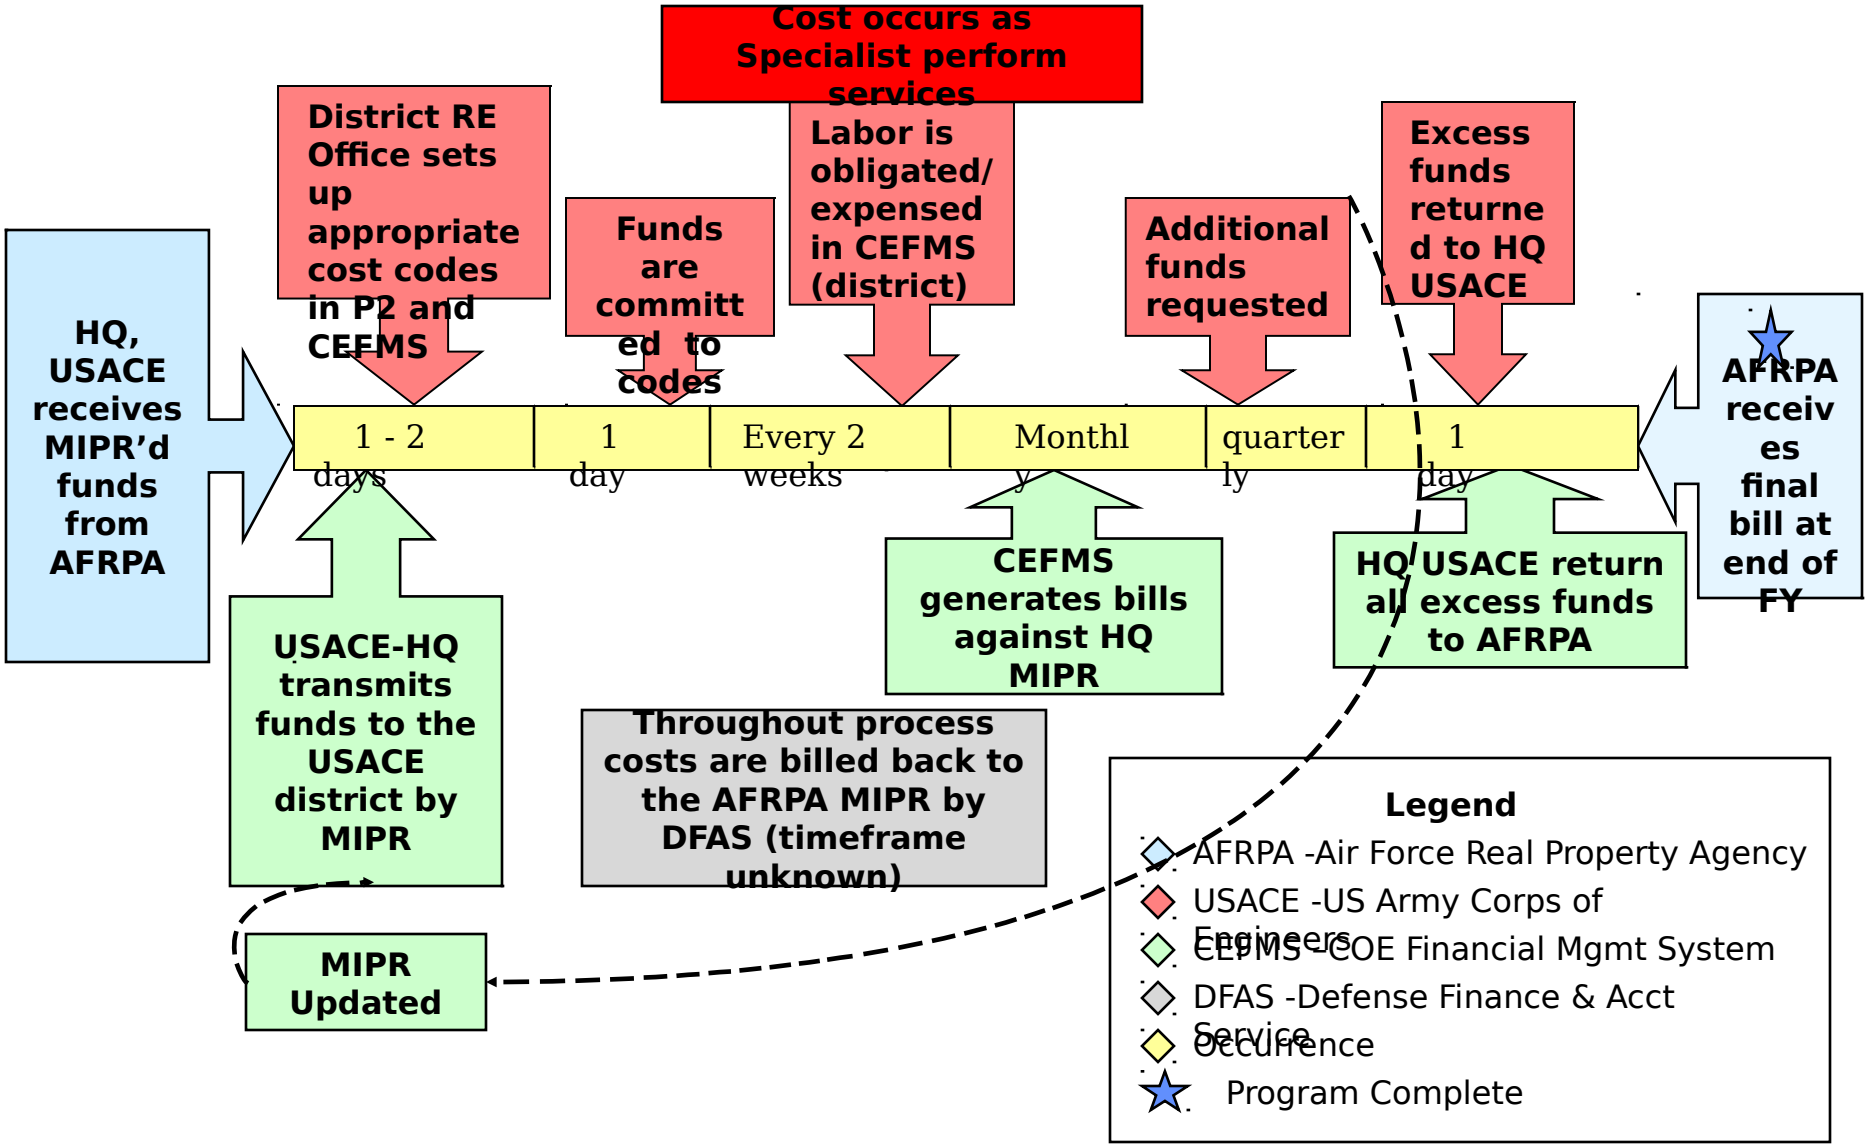
Cost occurs as Specialist perform services
District RE Office sets up appropriate cost codes in P2 and CEFMS
Funds are committed to codes
Labor is obligated/ expensed in CEFMS (district)
Additional funds requested
Excess funds returned to HQ USACE
HQ, USACE receives MIPR'd funds from AFRPA
1 - 2 days
1 day
Every 2 weeks
Monthly
quarterly
1 day
AFRPA receives final bill at end of FY
USACE-HQ transmits funds to the USACE district by MIPR
CEFMS generates bills against HQ MIPR
HQ USACE return all excess funds to AFRPA
Throughout process costs are billed back to the AFRPA MIPR by DFAS (timeframe unknown)
MIPR Updated
Legend
AFRPA -Air Force Real Property Agency
USACE -US Army Corps of Engineers
CEFMS -COE Financial Mgmt System
DFAS -Defense Finance & Acct Service
Occurrence
Program Complete

Air Force Action Timeline
Legislated Disposals

ALASKA DISTRICT

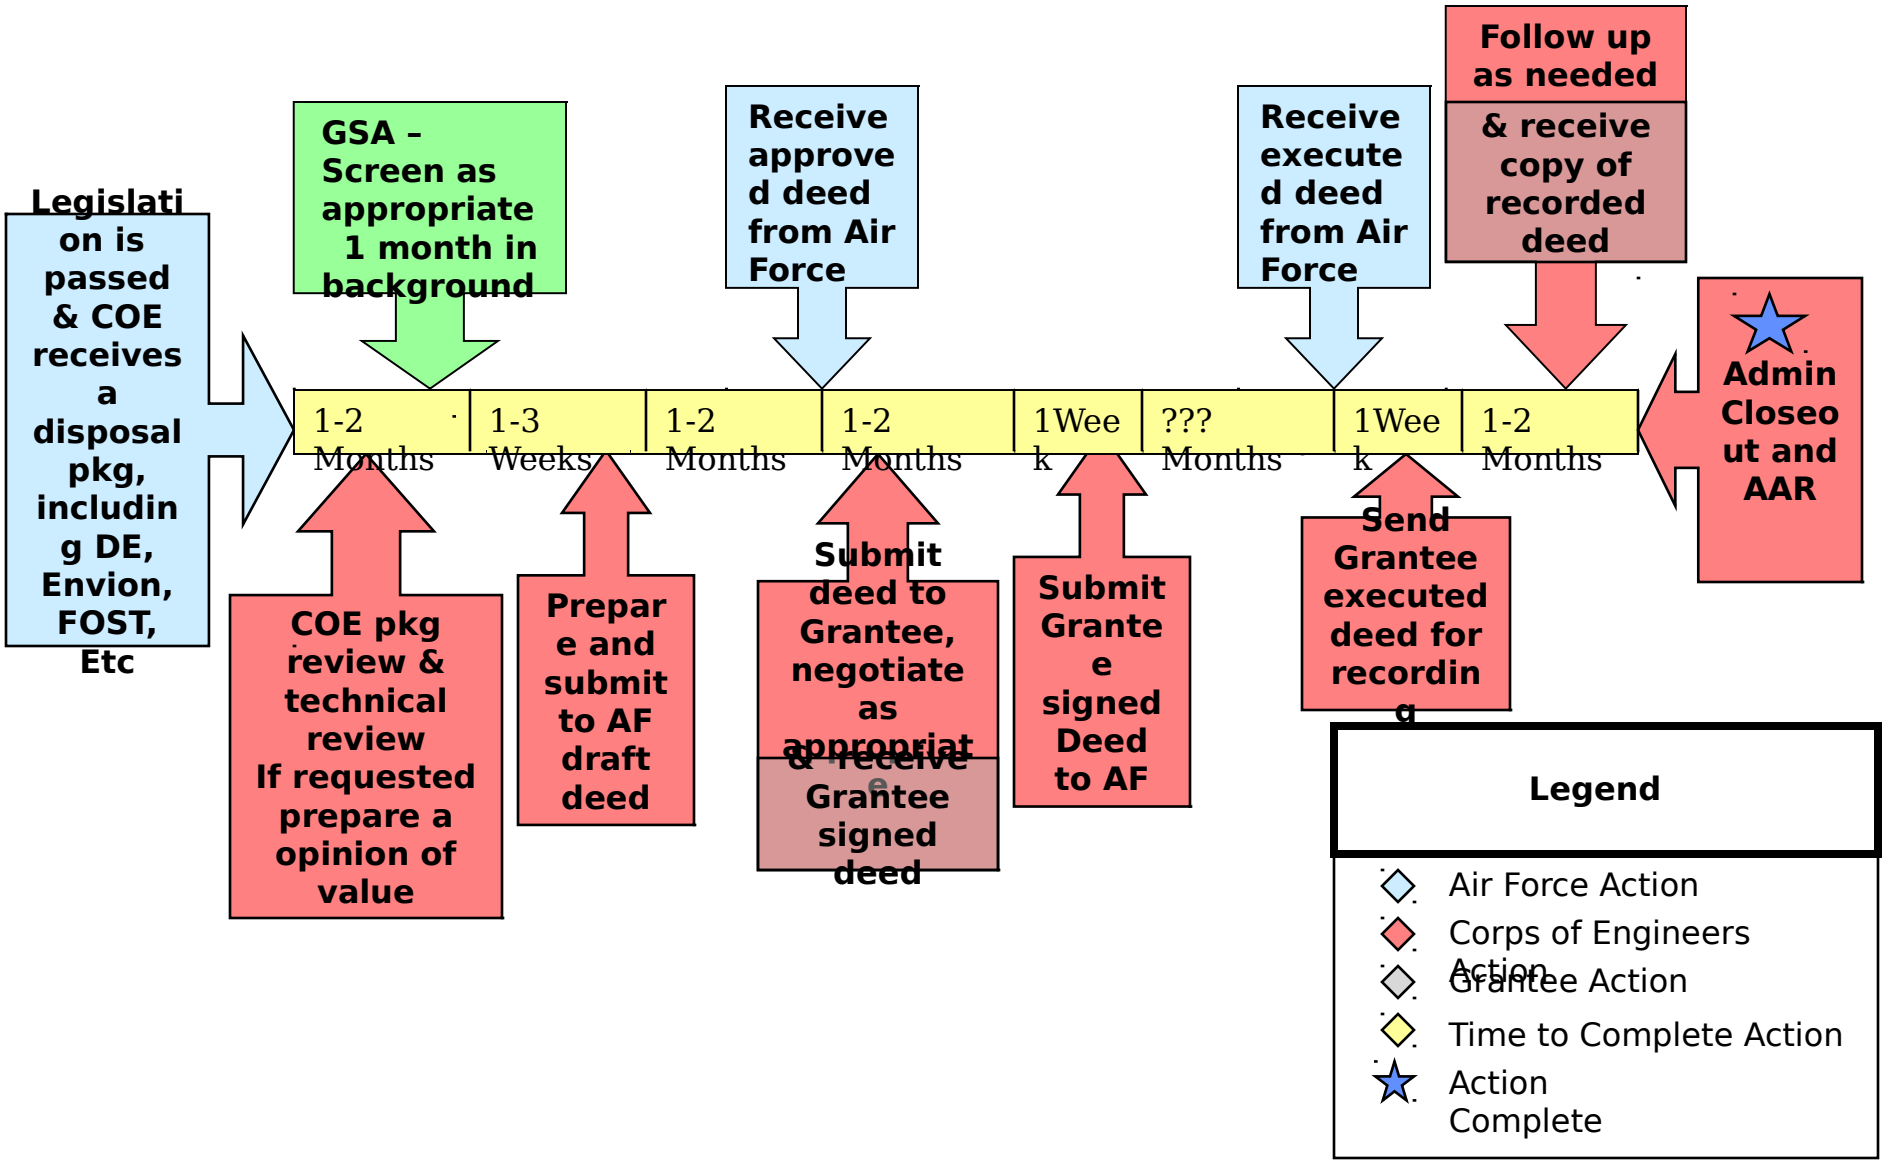
Legislation is passed & COE receives a disposal pkg, including DE, Envion, FOST, Etc
GSA – Screen as appropriate 1 month in background
Receive approved deed from Air Force
Receive executed deed from Air Force
Follow up as needed
& receive copy of recorded deed
Admin Closeout and AAR
1-2 Months
1-3 Weeks
1-2 Months
1-2 Months
1Week
??? Months
1Week
1-2 Months
COE pkg review & technical review If requested prepare a opinion of value
Prepare and submit to AF draft deed
Submit deed to Grantee, negotiate as appropriate & receive Grantee signed deed
Submit Grantee signed Deed to AF
Send Grantee executed deed for recording
Legend
Air Force Action
Corps of Engineers Action
Grantee Action
Time to Complete Action
Action Complete

Air Force Action Timeline
Legislated Disposals
COE Prepares DE Pkg

ALASKA DISTRICT

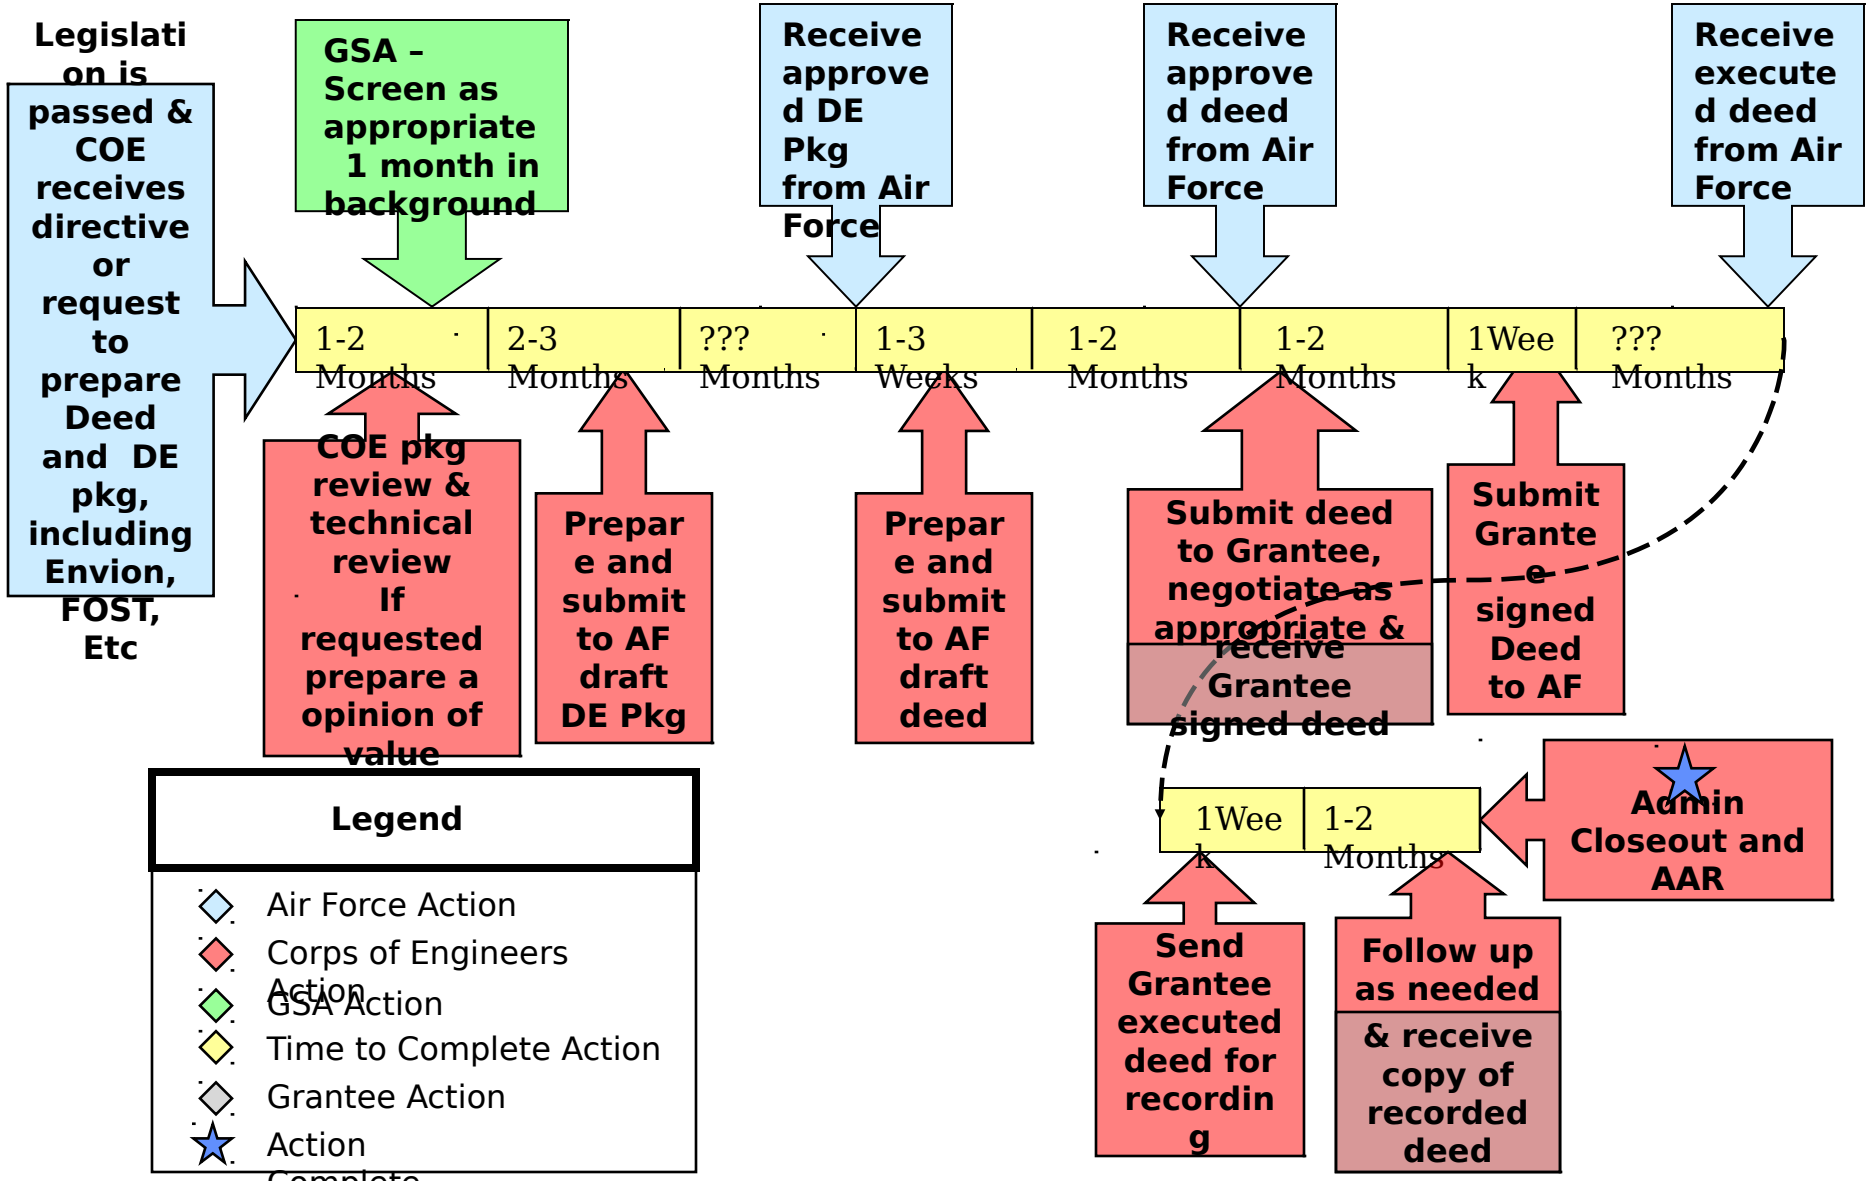
Legislation is passed & COE receives directive or request to prepare Deed and DE pkg, including Envion, FOST, Etc
GSA – Screen as appropriate 1 month in background
Receive approved DE Pkg from Air Force
Receive approved deed from Air Force
Receive executed deed from Air Force
1-2 Months
2-3 Months
??? Months
1-3 Weeks
1-2 Months
1-2 Months
1Week
??? Months
COE pkg review & technical review If requested prepare a opinion of value
Prepare and submit to AF draft DE Pkg
Prepare and submit to AF draft deed
Submit deed to Grantee, negotiate as appropriate & receive Grantee signed deed
Submit Grantee signed Deed to AF
1Week
1-2 Months
Admin Closeout and AAR
Send Grantee executed deed for recording
Follow up as needed & receive copy of recorded deed
Legend
Air Force Action
Corps of Engineers Action
GSA Action
Time to Complete Action
Grantee Action
Action Complete

Air Force Action Timeline
Outgrants – Renewals

ALASKA DISTRICT

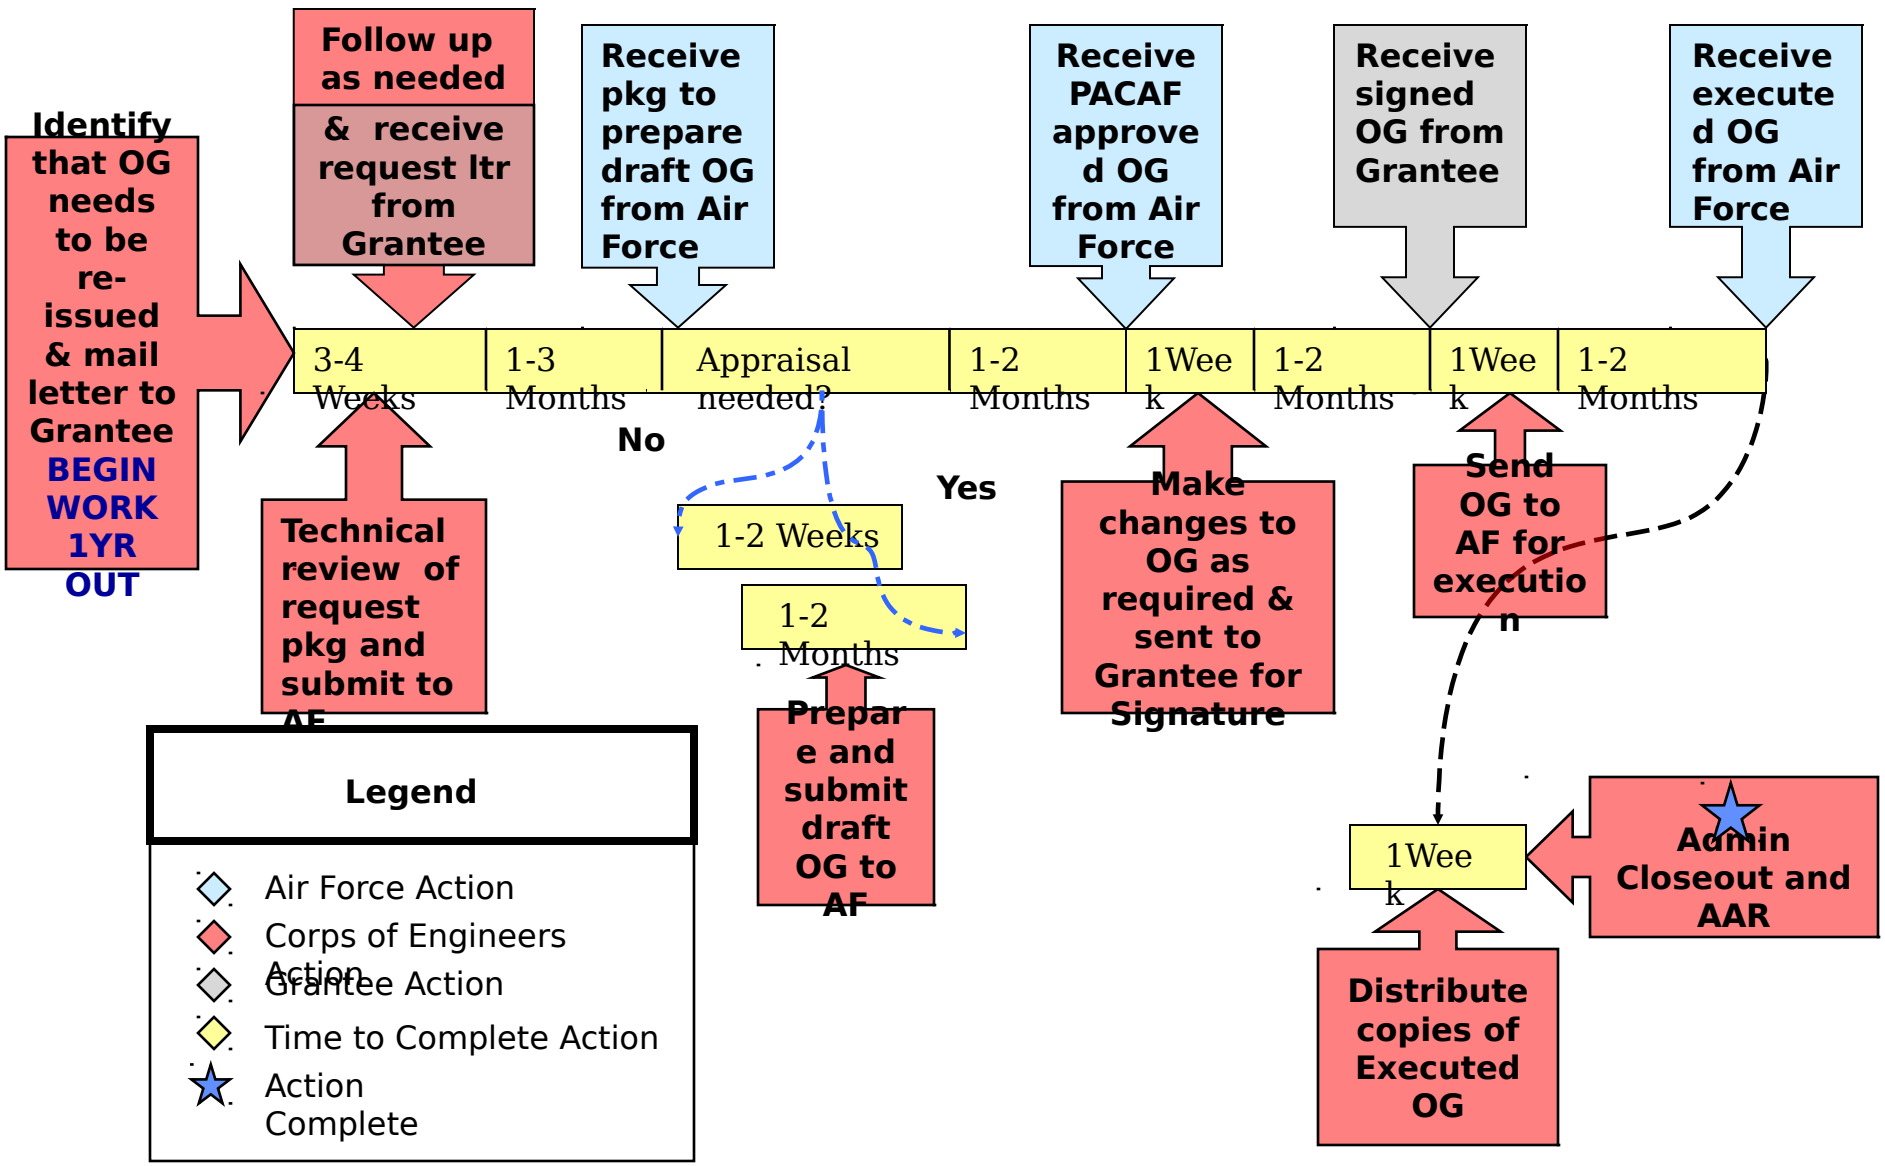
Identify that OG needs to be re-issued & mail letter to Grantee BEGIN WORK 1YR OUT
Follow up as needed & receive request ltr from Grantee
Receive pkg to prepare draft OG from Air Force
Receive PACAF approved OG from Air Force
Receive signed OG from Grantee
Receive executed OG from Air Force
3-4 Weeks
1-3 Months
Appraisal needed?
1-2 Months
1Week
1-2 Months
1Week
1-2 Months
No
Yes
Technical review of request pkg and submit to AF
1-2 Weeks
1-2 Months
Prepare and submit draft OG to AF
Make changes to OG as required & sent to Grantee for Signature
Send OG to AF for execution
1Week
Admin Closeout and AAR
Distribute copies of Executed OG
Legend
Air Force Action
Corps of Engineers Action
Grantee Action
Time to Complete Action
Action Complete

Air Force Action Timeline

Outgrants – New

Grantee Requested

AK ALASKA DISTRICT

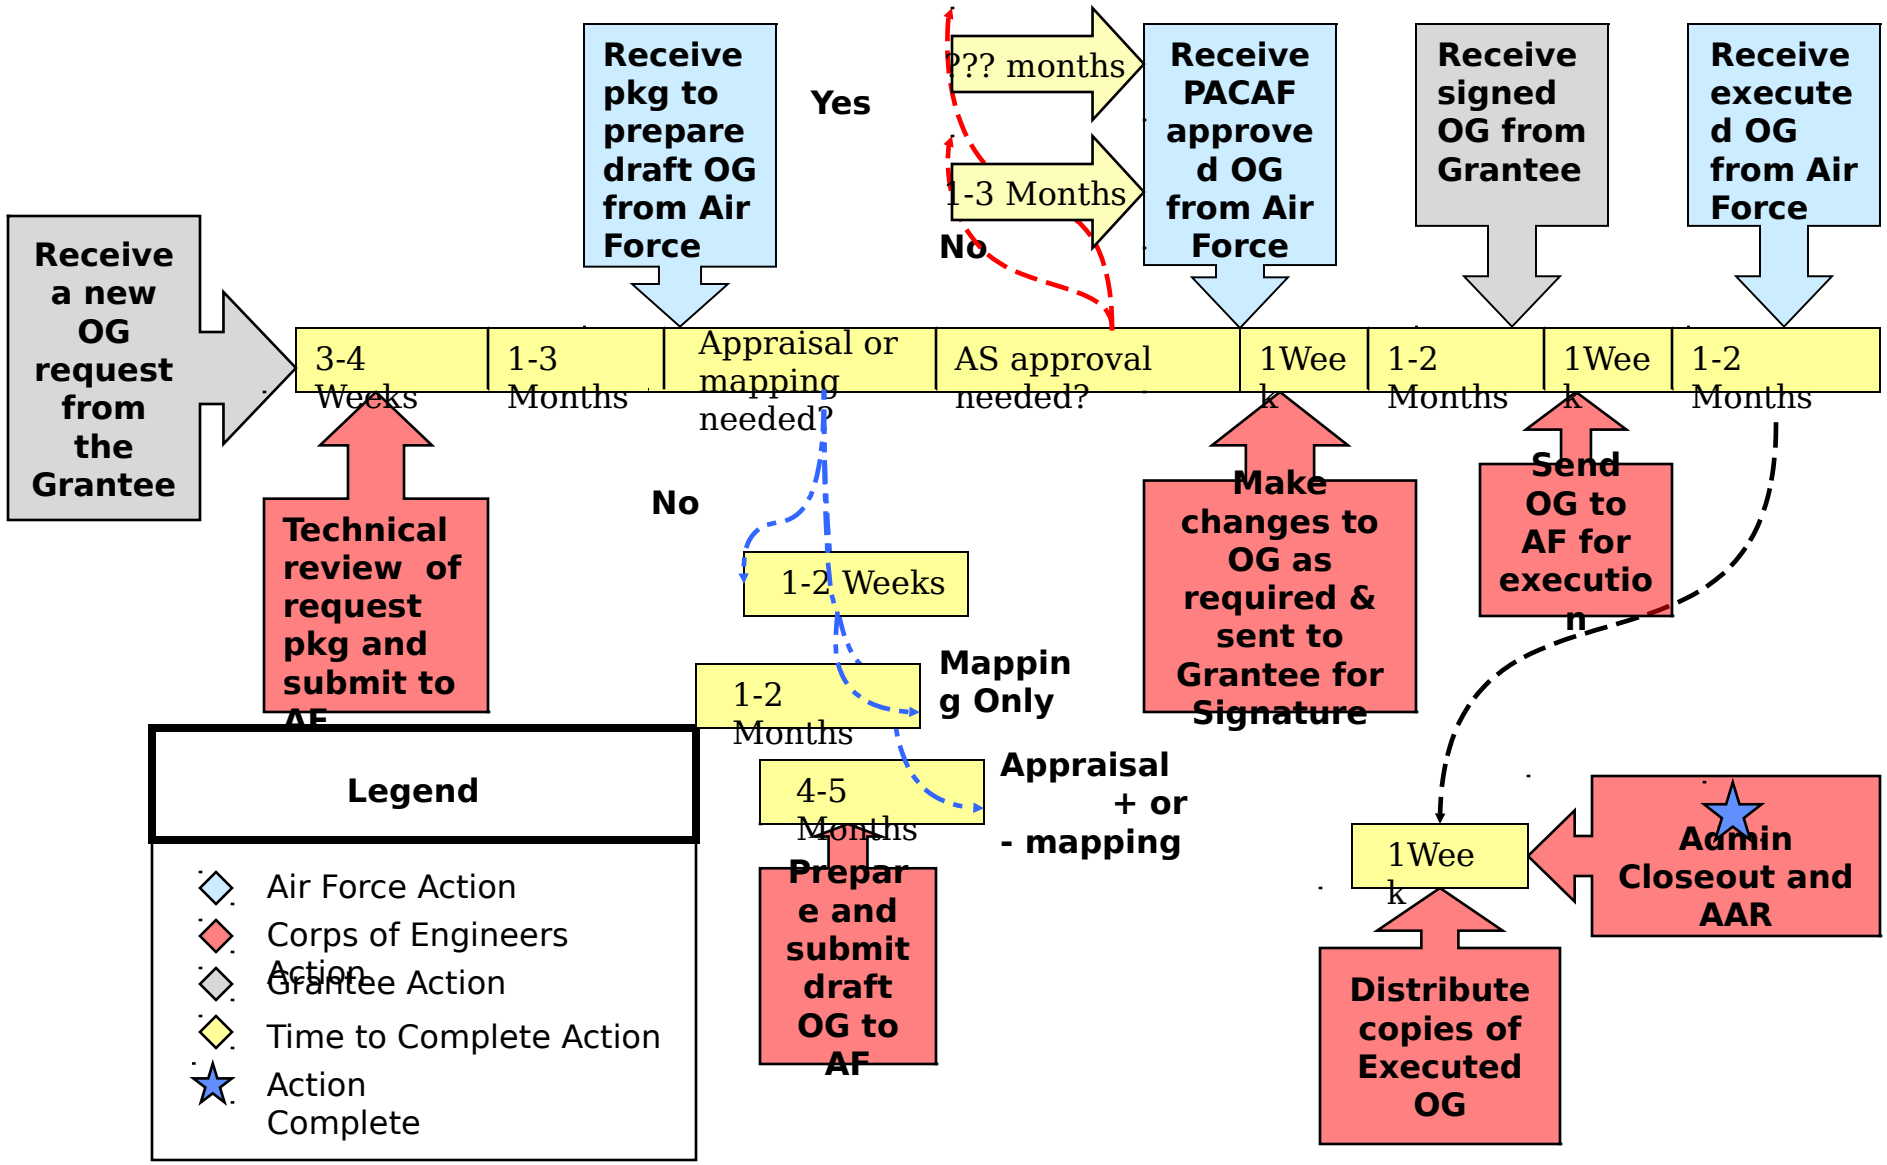

Air Force Action Timeline

Outgrants – New

Grantor Requested

AK ALASKA DISTRICT

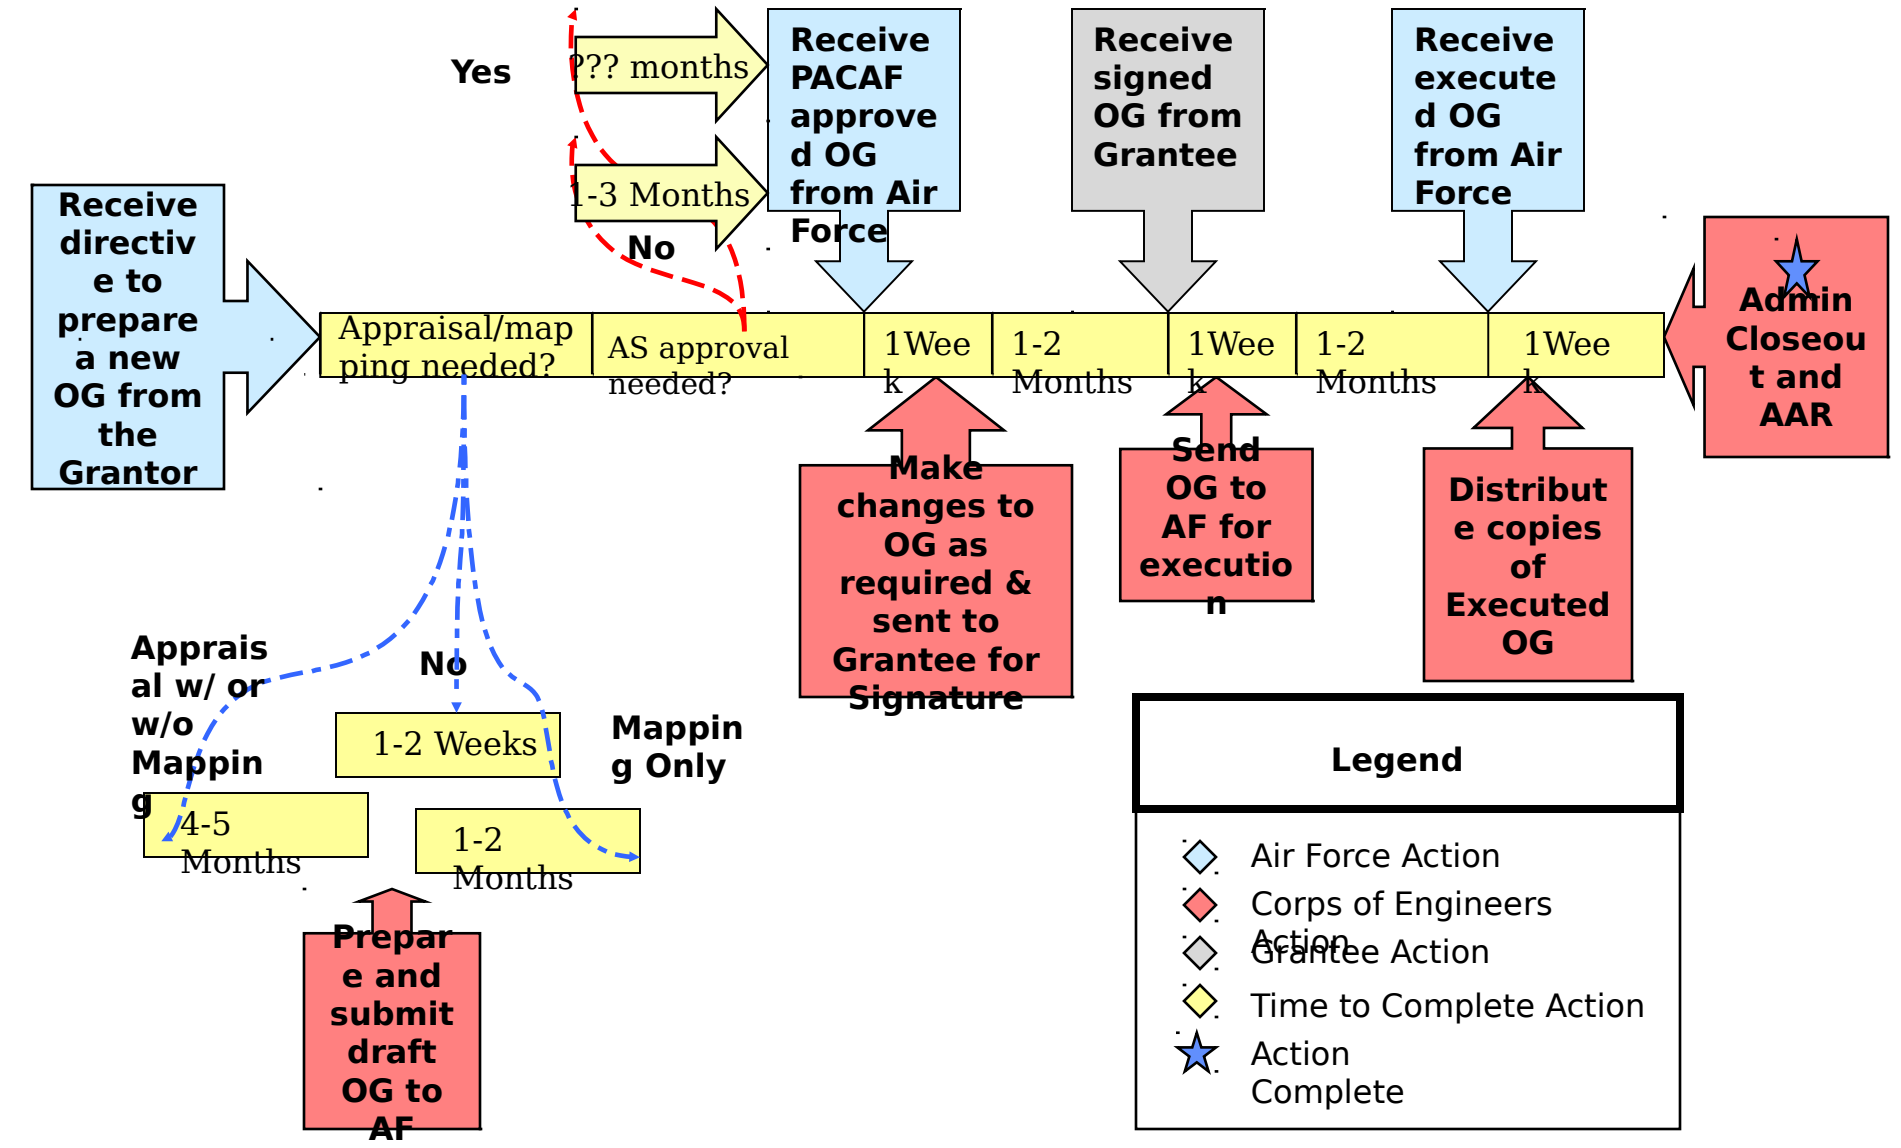

Air Force Action Timeline
Outgrants - Amendments

ALASKA DISTRICT

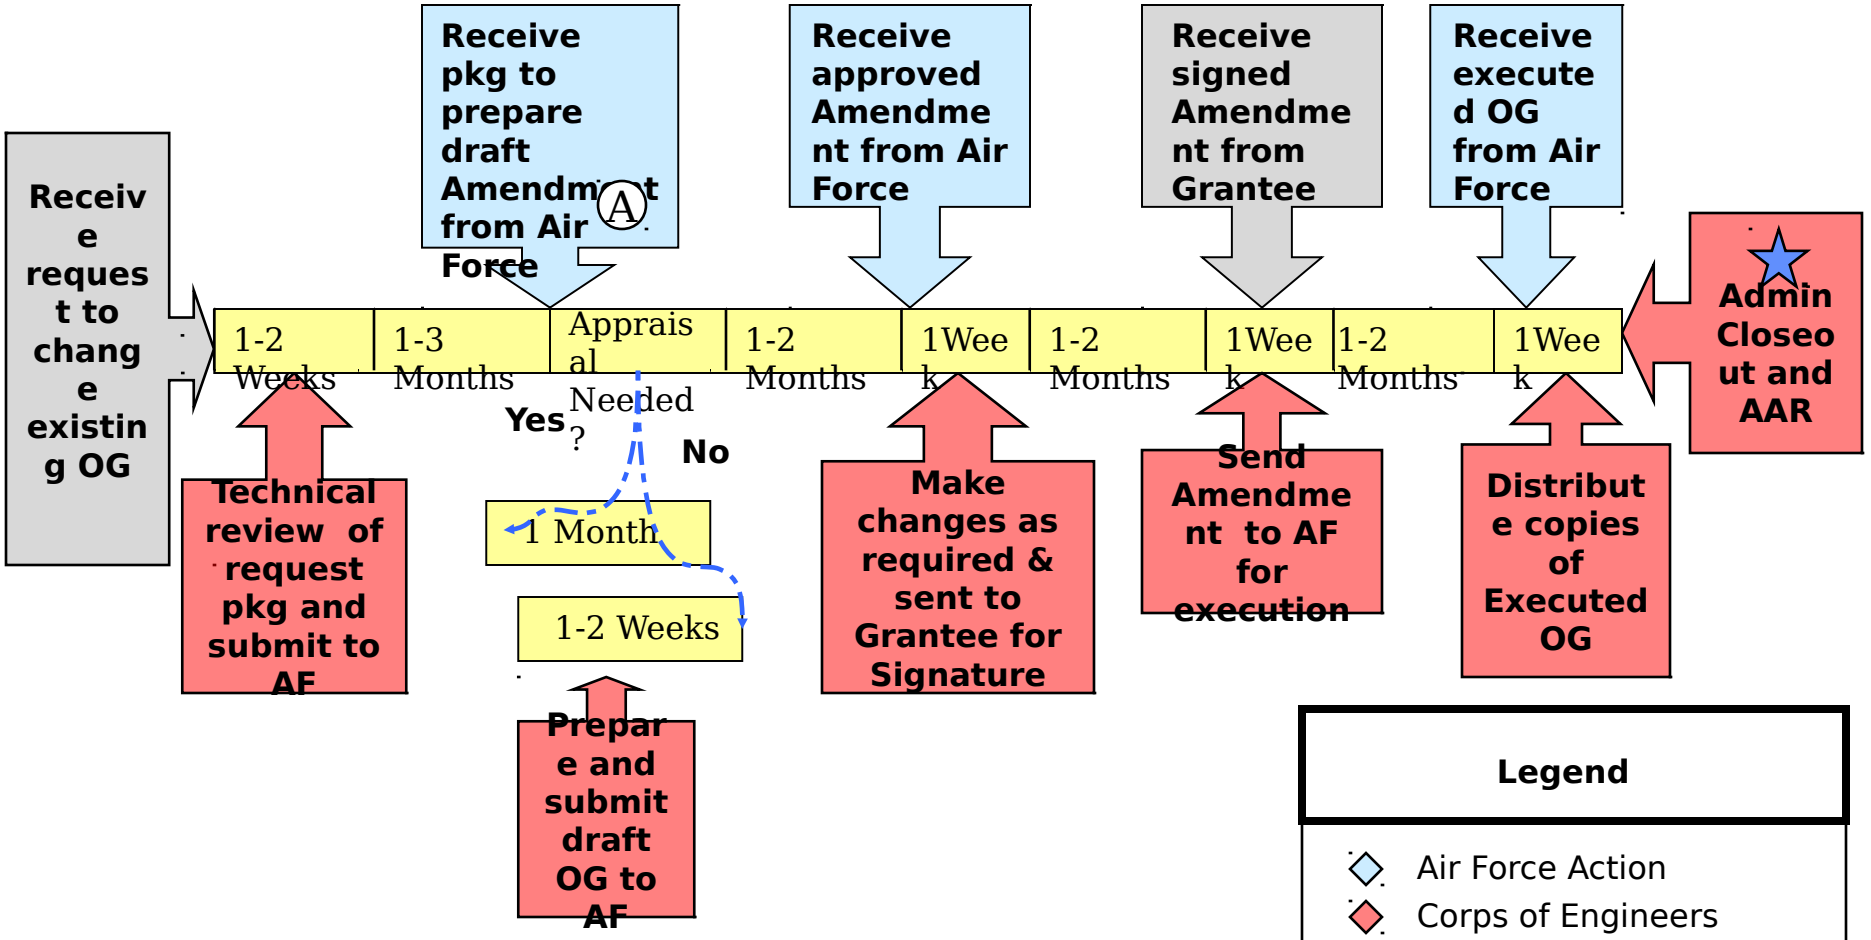
Receive request to change existing OG
Technical review of request pkg and submit to AF
1-2 Weeks
Receive pkg to prepare draft Amendment from Air Force Ⓐ
1-3 Months
Appraisal Needed?
Yes
No
1 Month
1-2 Weeks
Prepare and submit draft OG to AF
Receive approved Amendment from Air Force
1-2 Months
Make changes as required & sent to Grantee for Signature
1Week
Receive signed Amendment from Grantee
1-2 Months
Send Amendment to AF for execution
1Week
Receive executed OG from Air Force
1-2 Months
Distribute copies of Executed OG
1Week
Admin Closeout and AAR

Ⓐ If Grantor requested Action, begin time line here

Legend

- Air Force Action
- Corps of Engineers Action
- Grantee Action
- Time to Complete Action
- Action Complete

Air Force Action Timeline
Air Force Issued Outgrants

ALASKA DISTRICT
